



Region Kalmar län  
TM2 utvecklingsprojekt  
status 2020-01-10

*Baby Don't Blame Me !*

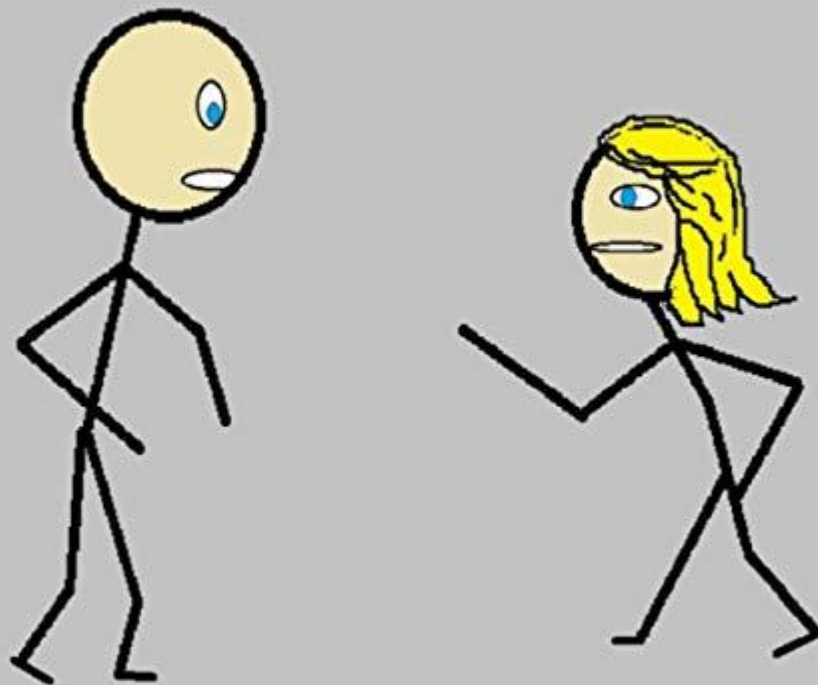

# New Time Schedule TM2 Release in 8.2.08

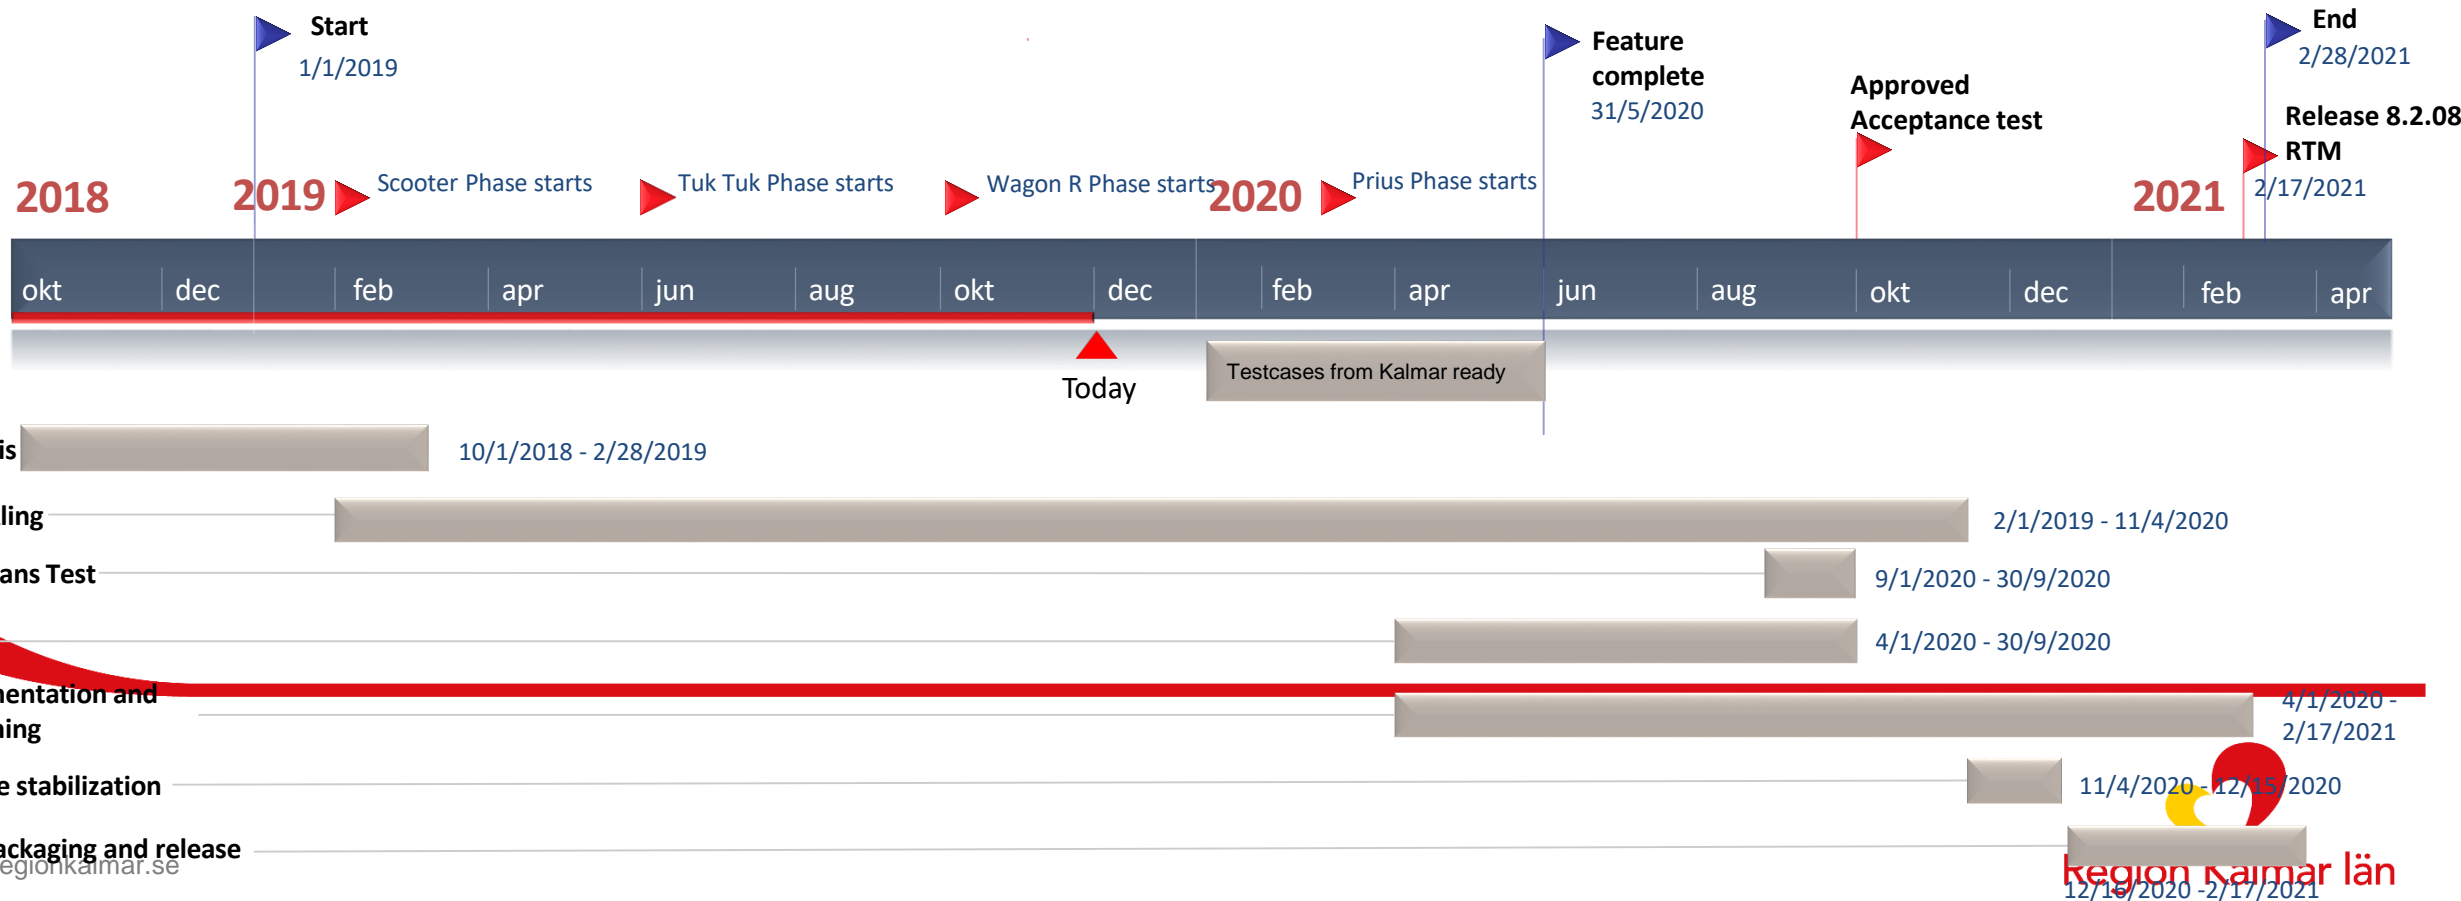

# TM2 utvecklingsprojekt

- Tidplan: 2019-01-01 - 2020-12-31
- Region Kalmar: acceptanskontrollör
- Övriga kunder deltar i projektstödsgrupper (rollbaserade grupper) och referensgrupp
- Design/utveckling: planeras klart 2020-05-31
- Acceptanstest: planeras klart 2020-09-30
- Justering/rättning: planeras klart 2020-12-31
- Leverans planeras till Cosmic Release 8.2.08 (mitten februari 2021)

# Status-plan

- Användningstester (enkla/övergripande koncept), utförda online i sbm rollbaserade möten
- Användartester utförda på plats:
  - Capio: oktober
  - Region Östergötland: oktober
  - Region Kalmar: november
- Användartester, planeras:
  - Karlstad preliminärt slutet av februari
  - Övriga kunder....ska planeras
- Framtagandet av användarscenarier/testscenarier startar nu (Kalmar) - ska användas vid acceptanstest. Ska täcka olika behov/olika typer av verksamhet/olika storlek på sjukhus etc
- Avstämning kommer att ske med övriga kunder.

## Lite mer konkret vad som händer just nu:

- Går över från "enstycks-funktioner till flöden (Cambio)
- Mer designarbete nu (Cambio)
- Mallstrukturer skapas för olika grundstenar, t ex op-anmälan (Cambio)
- Testmiljö från Cambio tillgänglig i slutet av mars
- Region Kalmar ska införa TM2 först av alla 😊
- Provpatienter skapas som ska testas
- Parallella projekt i Region Kalmar redan nu inför driftsättning:
  1. Hur avvecklas Optimera?
  2. Integration PDMS
  3. Hur ska införandet gå till?
  4. Skapar mallar inför utbildning

Id	Area vs Phase	Scooter	Tuk-Tuk	Wagon R	Prius (MVP)	Comment
E01.1	Decide and prepare elective case	Completed	Completed	InProgress	Not started	
E01.2	Read and update Procedure case details	Completed	Completed	InProgress	n/a	
E01.3	See and handle related Activities	n/a	n/a	InProgress	Not started	
E01.4	See and handle Patient details	n/a	n/a	InProgress	n/a	
E01.5	Communicate with colleagues regarding the case	n/a	n/a		Not started	
E02.1	Create booking incl all requested resources	Completed	Completed	InProgress	Not started	
E02.2	Reschedule and Cancel	n/a	n/a		n/a	
E02.3	Communicate operation date (time)	n/a	Completed	Not started	Not started	
E03.1	Operation List	n/a	Completed	InProgress	Not started	
E03.2	Graphic schedule	Completed	Completed	InProgress	n/a	
E04.1	Plan theatre day program	n/a	Completed	InProgress	Not started	
E04.2	Plan tomorrows program	n/a	n/a	InProgress	Not started	
E05.1	Monitor status and manage program	Completed	Completed	InProgress	n/a	
E05.2	Handle Emergency cases	Completed	InProgress	Not started	n/a	
E05.3	Manage Anaesthetic interventions	n/a	InProgress	n/a	n/a	
E06.2	Perform and document preop activities (at the ward/reception)	n/a	n/a	InProgress	n/a	
E07.1	Create anaesthetic assessment	n/a	InProgress	Not started	n/a	
E07.3	Prepare for anesthetic day of anesthetic	n/a	n/a	Not Started	n/a	
E11.1	Register details about op	n/a	n/a	InProgress	n/a	
E11.2	Register details about anaesthetic	n/a	Completed	InProgress	Not started	
E11.3	Register waypoints	n/a	Completed	InProgress	Not started	
E11.4	Documentation for further care	n/a	n/a	InProgress	n/a	
E14	Settings and Selections	n/a	Completed	InProgress	n/a	
E15.2	Scan barcode to Procedure	n/a	n/a	n/a	Not started	
E17.1	Follow up the daily work	n/a	n/a	Not started	n/a	
E20	Surgery capacity	n/a	n/a			
E21	Resource administration	n/a	Completed		n/a	
E22	Rules			Not started		
E23	Templates and components	n/a	Completed	InProgress	n/a	

# "Dashboard" (ärendeöversikt)

The screenshot shows the 'Theater Management Window' for patient Kennedy Amber, 24 yo, with Case ID: 123456. The patient's contact is Beatrice Hammond, and the priority is Electiv, 3 months. The date is 2019-12-28, and the current phase is Planning. The process flow includes: Surgery registration (Created), Booked (Time confirmed), Anaesthetic assessment (Done), Planning, Preop, Surgery, and Postop. The main workspace is divided into several panels: 'Surgery registration', 'Anaesthetic', 'Post-op', 'Patient administration', and 'Todo'. A search bar and a '+ ' button are also visible.

Olika ytor för respektive område

- Operationen
  - Anmälan
  - Op-journal
- Anestesi
  - An-bedömning
  - An-journal
- Planering/patientadmin
- Att-göra
- ...

"Mini-patientöversikt"



Mini-patientöversikt

- Fälls fram för att visa ytterligare patientinformation från olika delar av COSMIC







**Tillsammans**  
för ett **friskare**  
**tryggare** och  
**rikare liv**
